



DARK ENERGY
Survey



Fermilab

Dark Energy Survey (DES) DECam Project Working Group Meeting

October 06, 2006

10:00 – 12:00 Noon

Black Hole

Agenda


- 1) HQ Interactions: Feedback on Discussions with Headquarters [Mont/Brenna/John]
- 2) Feedback as appropriate on Mont's Oct. 3 teleconference with Dunning and Mould [John]
- 3) Presentation on Procurement "Guidelines and Cycle times" [Joe Collins – Procurement]
- 4) Requisition Approval/Signoff Thresholds/Process [Dean]
- 5) Timeline [Ed/Dean]
- 6) DES-DECam Status / Progress on All CD-1 Documentation [Wyatt/Brenna]
- 7) Status of Action Items [Brenna/Wyatt]



Dark Energy Survey - DECam Project Timeline for Critical Decisions & Reviews



Updated 20-Sep-06

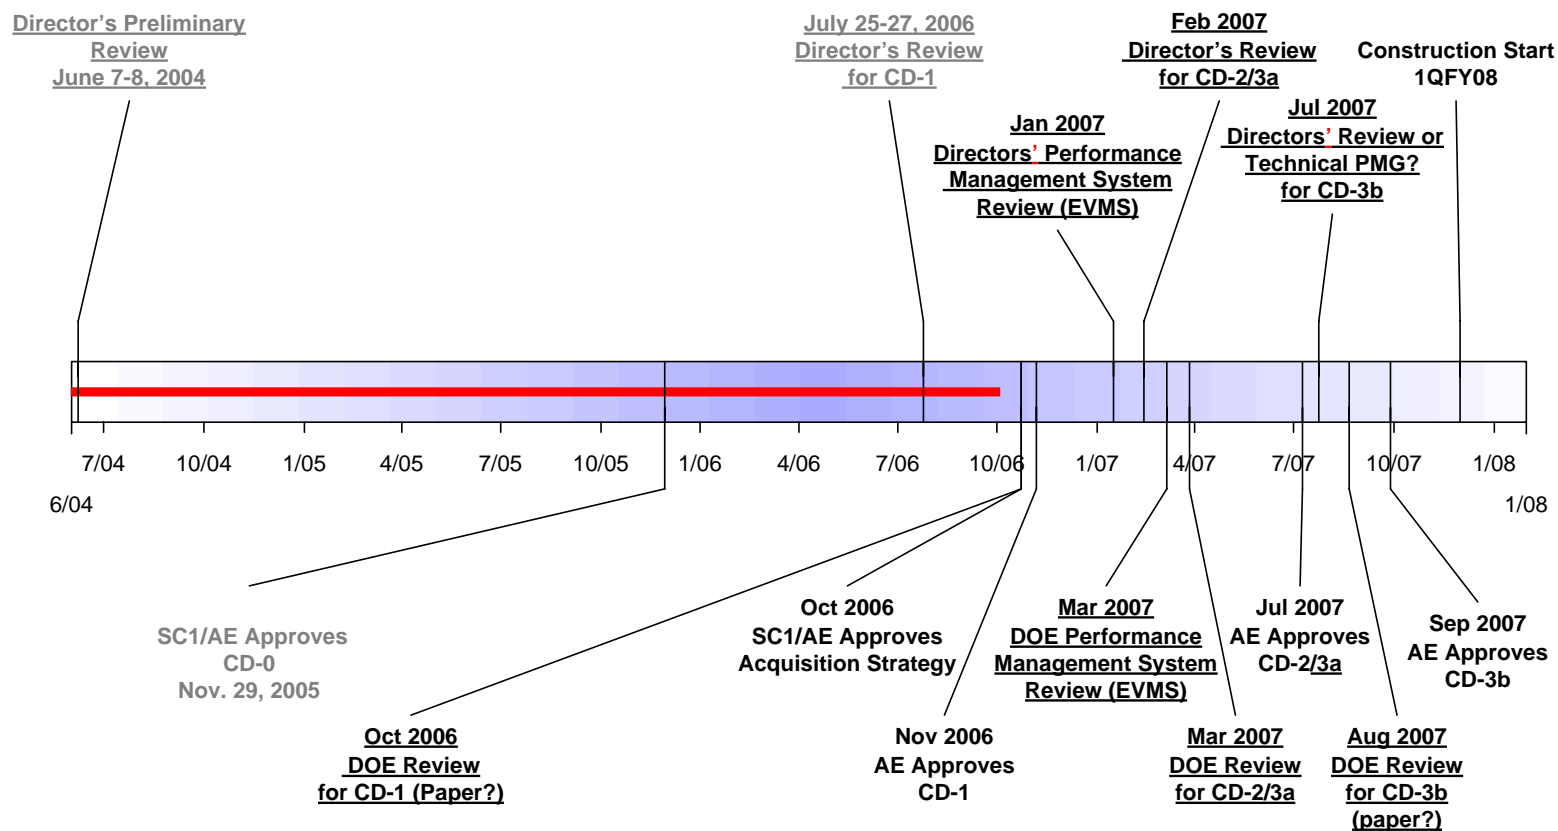




Dark Energy Survey – DECam Project Draft Critical Decisions Prerequisites



Updated 12-Sep-06

Estimated Need by Dates
for DOE Approvals
and Documents

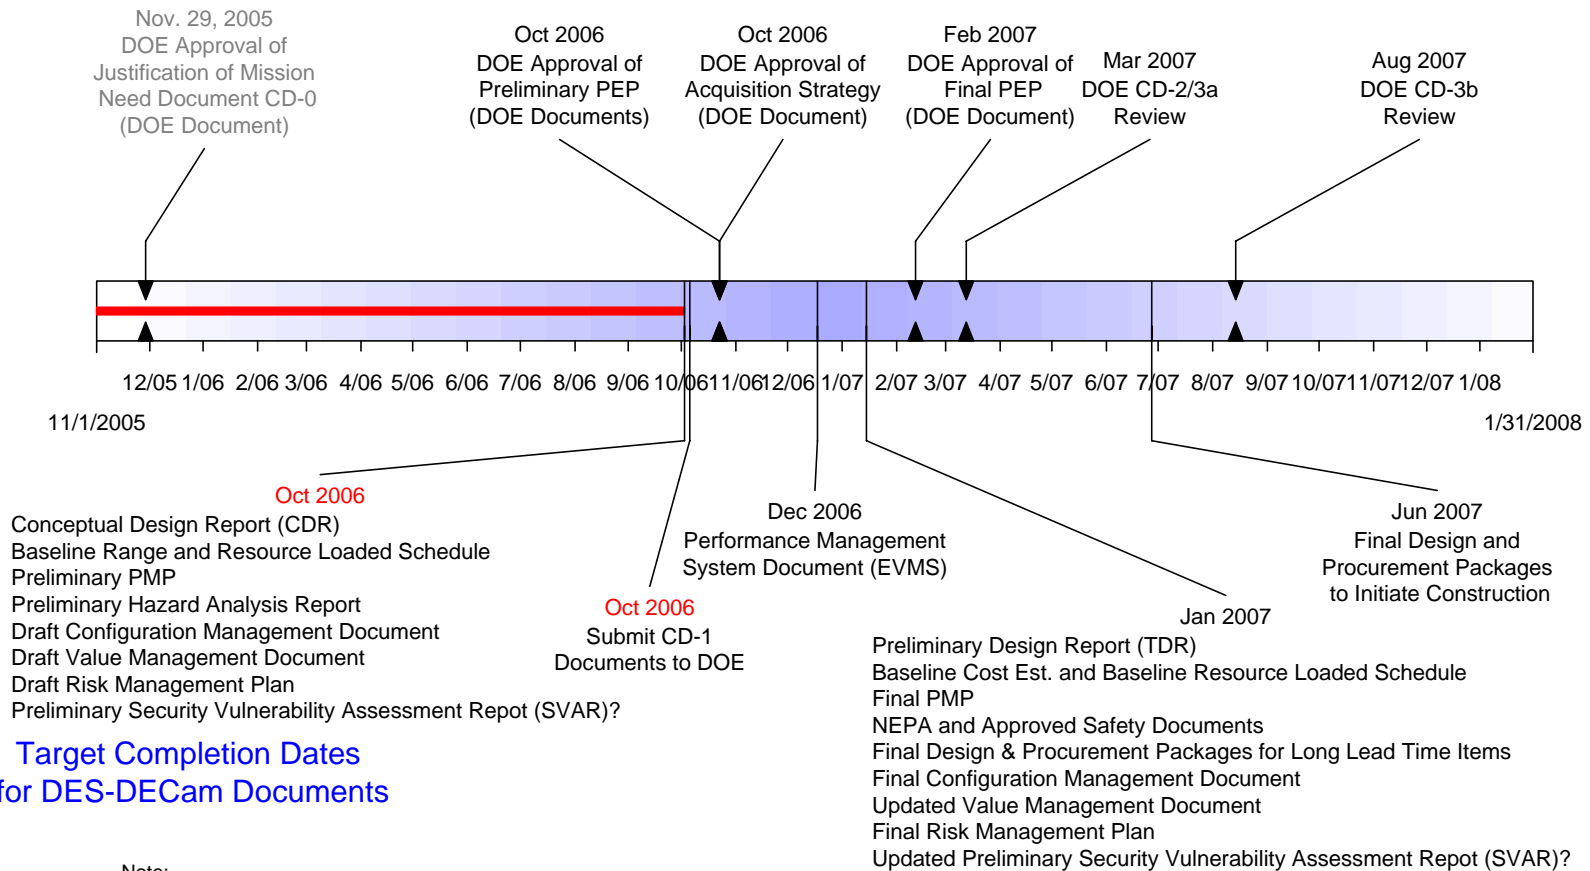

Target Completion Dates
for DES-DECam Documents

Note:
Items marked in Red indicates change from prior version

Action Items

New:

- a) Status progress on the determination if a Preliminary Security Vulnerability Assessment Report (SVAR) is applicable to the DES-DECam project. [Paul]

Carryover:

- b) Status on proposal for the start date which R&D is to be tracked and reported on as part of the TPC. Need to determine prior to final submittal of the CD-1 documentation to DOE. [Brenna/Wyatt]
- c) Complete response to recent Director's Review and send to the Associate Director. Make it available on the OPMO website for Kathy to access if she so chooses. [Brenna]
- d) Give latest PPMP to OPMO (Ed/Dean), Jim Strait, and Greg Bock to review and feed back any recommended changes prior to CD1 documentation submittal to DOE. [Brenna/Wyatt]
- e) Inform the DECam project on the final decision regarding the format of the DOE CD-1 review (paper review or otherwise). [Paul]
