



# NOvA Working Group Meeting

September 07, 2005

2:00 – 4:00 PM

Snake Pit


# Agenda

- 1) Feedback on interchanges between the Directorate and OHEP [Mont]
- 2) NOvA Progress Report [John Cooper]
- 3) Ash River & Orr-Buyck Site Visits [Steve Dixon]
- 4) Review NOvA Timeline [Ed Temple]
- 5) Status on Preparation of Project Documents [Ron Ray]
- 6) Presentation on Value Engineering [Ed Crumpley]
- 7) Status of Action Items [John Cooper]



# DRAFT NOvA Project Timeline for Critical Decisions & Reviews

Updated 16-Aug-05

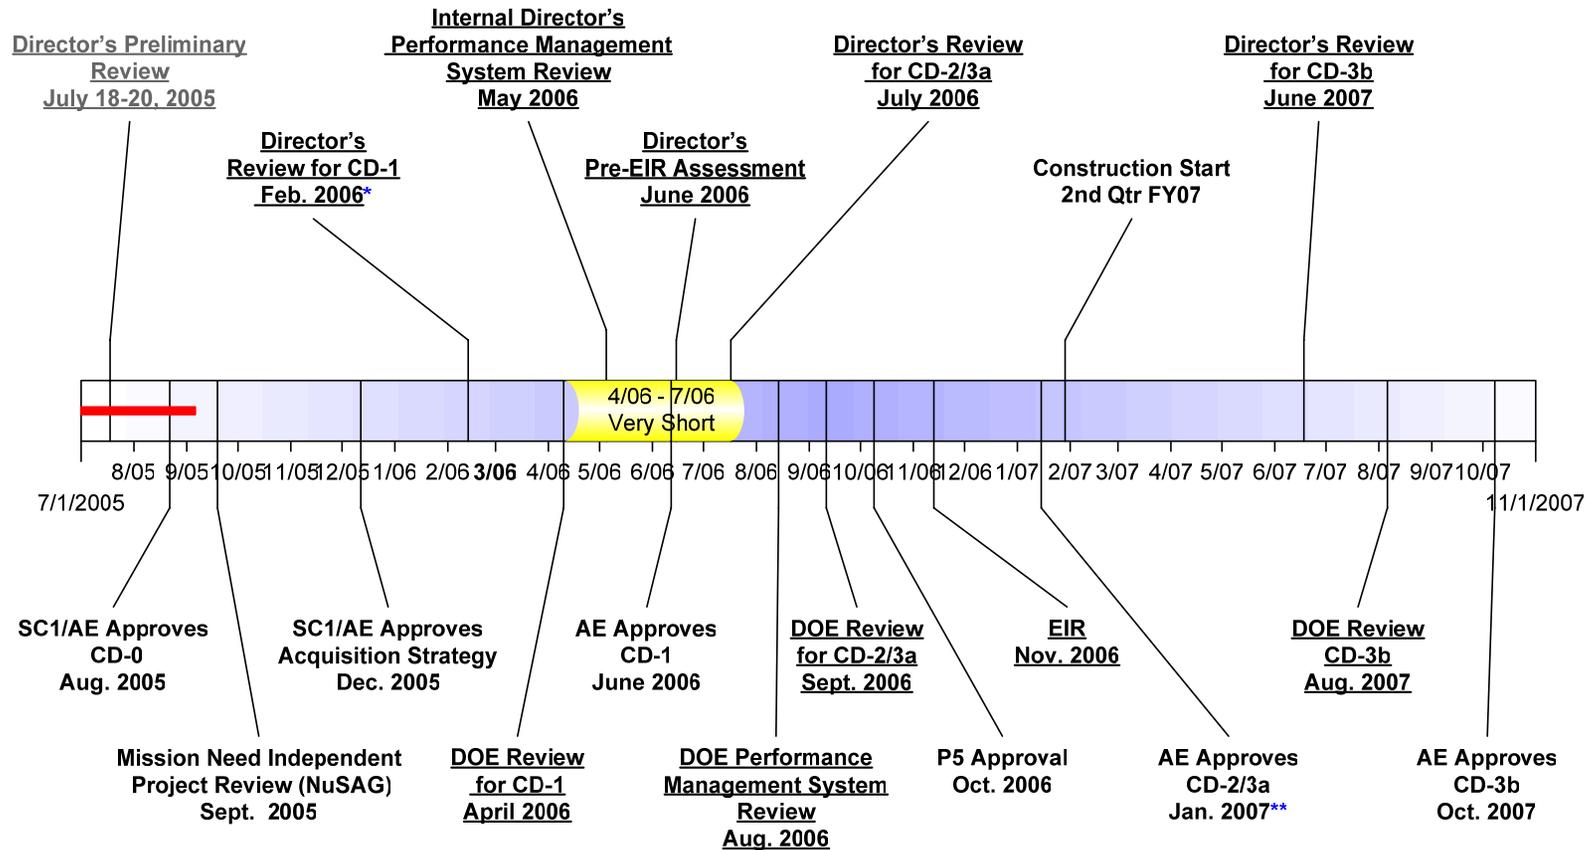

Note:

\* 6 months after L-2 Managers

\*\* 18 months after L-2 Managers

07-Sep-05

NOvA Working Group Meeting




# NOVA Project

## Draft Critical Design Prerequisites

Updated 16-Aug-05



### Estimated Need by Dates for DOE Approvals and Documents

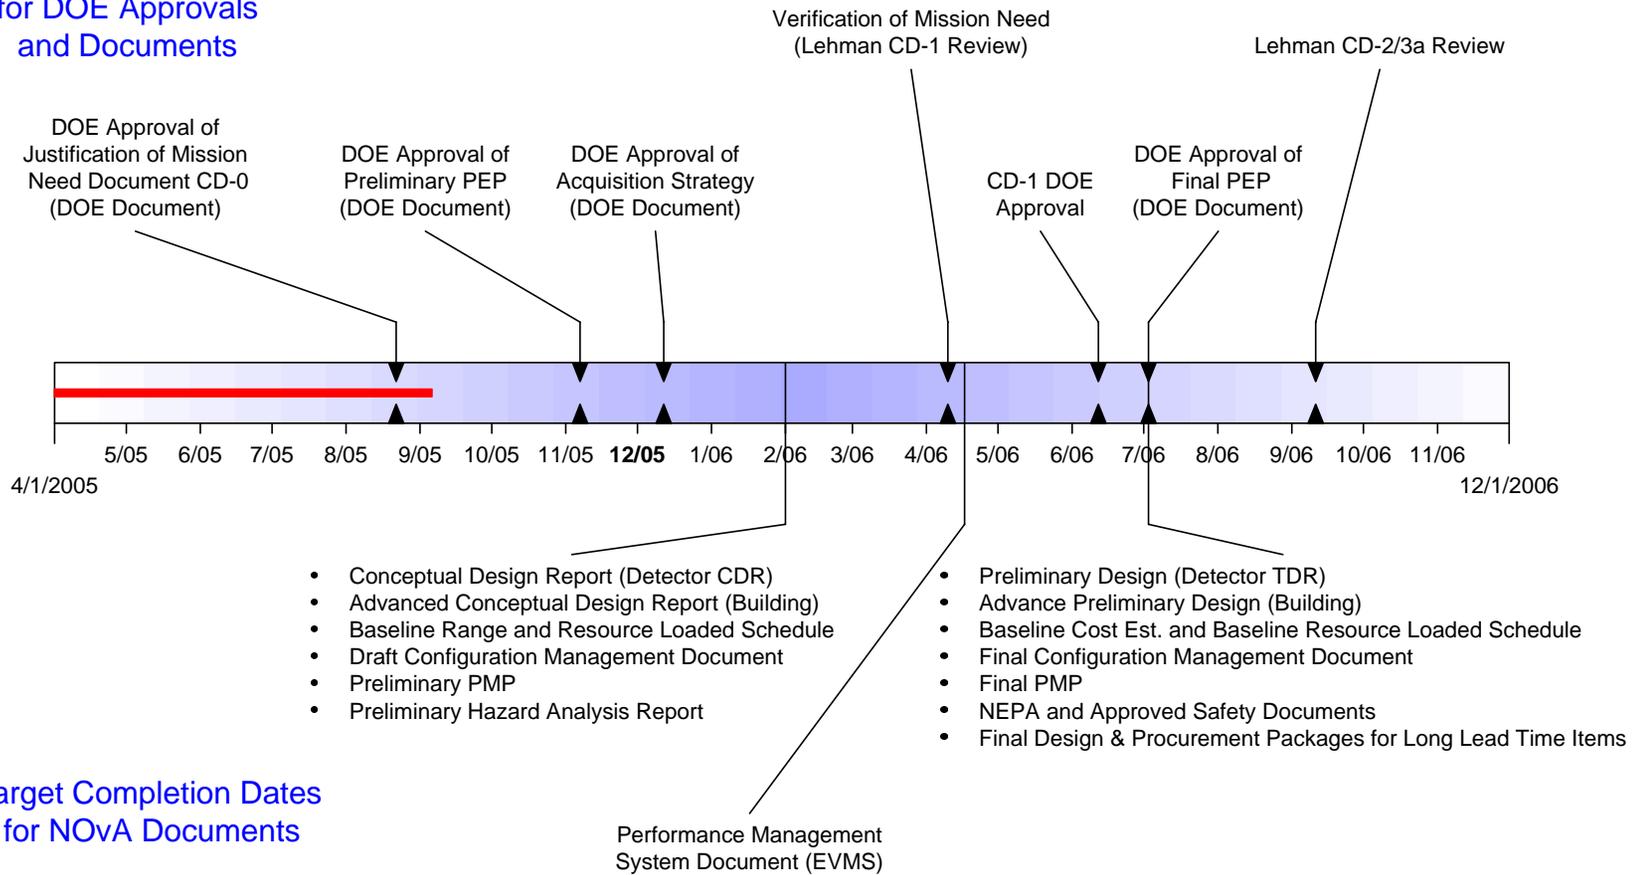

### Target Completion Dates for NOVA Documents

07-Sep-05

NOVA Working Group Meeting

# Open Action Items

- a) Provide paper describing the 2<sup>nd</sup> site (Orr-Buyck Rd) [Marshak]
- b) Kesich emailed Jon Cooper DOE and John Cooper recapping his interpretation of their discussion and requesting concurrence. Still waiting for a response. [Kesich, Webster]
- c) EAW Contractor awarded PO. Report on schedule for performing work. [Cooper]
- d) Continue development of WBS.
- e) Directorate to formally appoint NOvA Project Manager and concur with Deputy. [Montgomery]
- f) NOvA/PPD Division Office to Plan, Schedule and move NOvA Project Office to 13NW. [Strait/Crisler & Cooper]
- g) Staff administrative support person to support NOvA Project Office. [Strait & Phillips]
- h) Try to resolve how to handle funding options issue for the construction of the far site by the Oct/Nov timeframe [Cooper, Montgomery]

# Open Action Items (continued)

- i) Need feedback to/ (from?) Marvin Marshak on what kind of guarantee U of MN would want related to the far site construction if they proceed with their own \$\$ [Marshak, Cooper]
- j) Report on usability of NOvA's Document Database for Collaborators accessing information from reviews (talks, etc.) [Cooper]
- k) Need process/letters(?) to formally appoint L2 managers for R&D phase [Cooper]
- l) Continue developing documentation for acquisition strategy [Cooper/Ray with Lutha/Procario and FNAL procurement]
- m) NOvA Working Group Meeting participants to send to Mont suggested membership for NOvA PMG. [All]
- n) NOvA to supply Procurement the weighting of the criteria for evaluating bids for the 16 cell extrusion tooling. [Cooper]
- o) Discuss with Stan Wojcicki the potential for pursuing funding from NSF for NOvA. [Mont]
