



NOvA Working Group Meeting

March 06, 2007

10:30 AM – 12:00 Noon

Snake Pit


Agenda

- 1) Feedback on interchanges between the Directorate/Project and OHEP [Hugh Montgomery/ Steve Holmes/ John Cooper/ Mike Procario]
 - a) Budget
 - b) CD-1 ESAAB
- 2) Discuss Results of NOvA Near Detector Discussion at 20-Feb WGM and what are the Next Steps [Hugh Montgomery/ John Cooper]
- 3) NOvA Progress Report [John Cooper/Ron Ray/Nancy Grossman]
 - a) CD-1 Documentation Updates [John Cooper/ Nancy Grossman/ Pepin Carolan]
 - b) Pending Detector/ANU Integration Items [John Cooper/ Nancy Grossman]
 - c) Environmental Assessment [John Cooper/ Keith Schuh/ Sally Arnold]
 - d) Cooperative Agreement [Mike Procario/ Pepin Carolan/ Steve Webster]
 - e) Status of Acquiring Additional Project Personnel. [John Cooper/Jim Strait]
- 4) Discussion on Scheduling Director's and DOE's CD- 2/3a Review [Dean Hoffer]
- 5) Review of Timeline [Dean Hoffer]
- 6) Status of Action Items [John Cooper]



DRAFT NOvA Project Timeline for Critical Decisions & Reviews


Updated 16-Jan-07

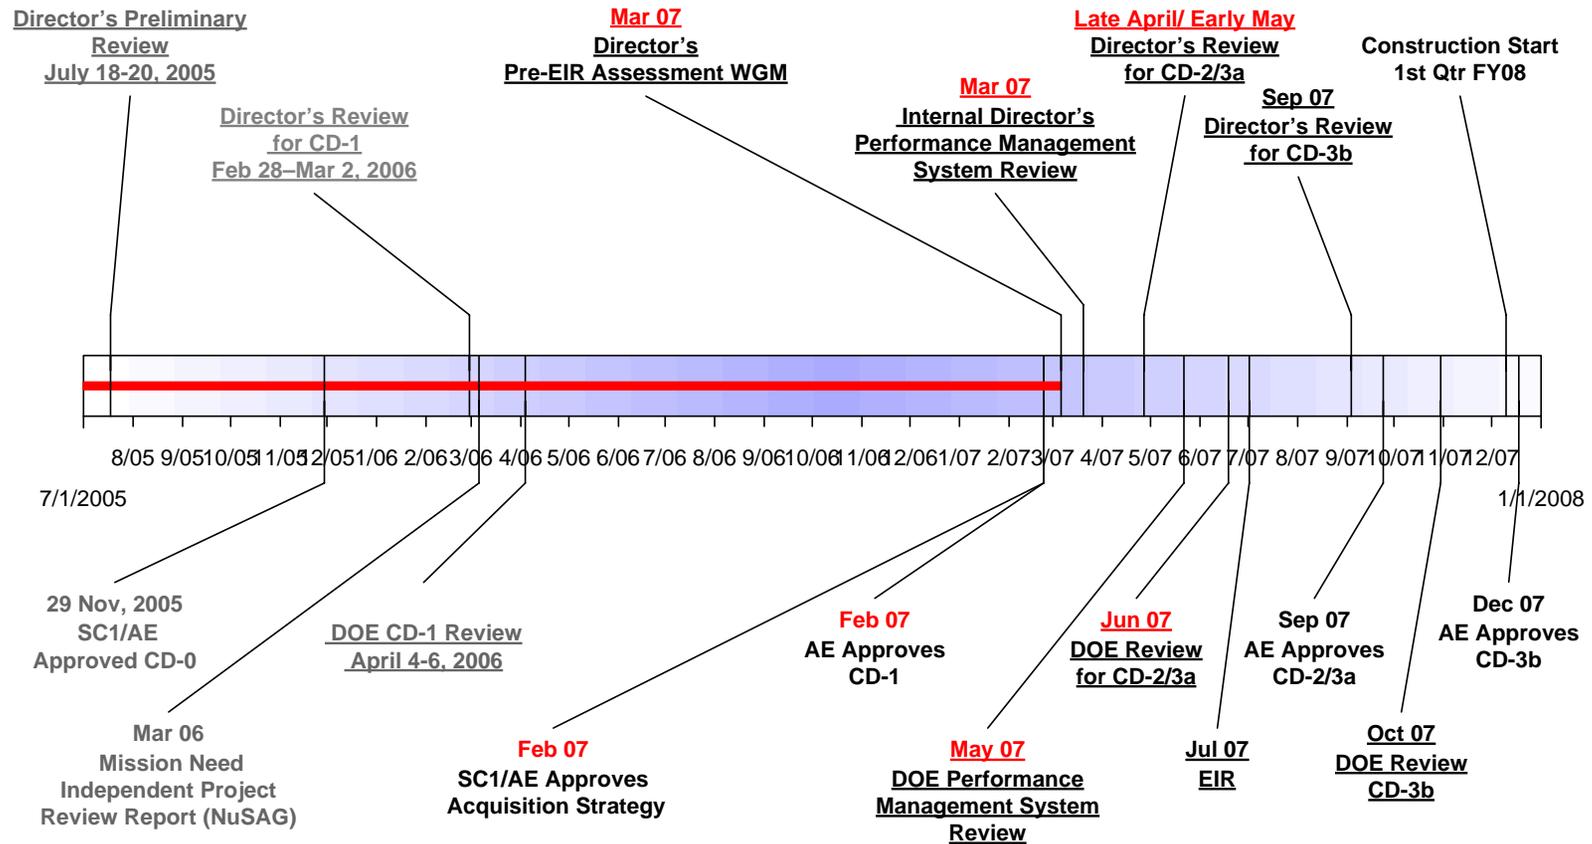

Note:

- Text in Red indicates change from prior version

EIR Process Timeline (Best Guess)

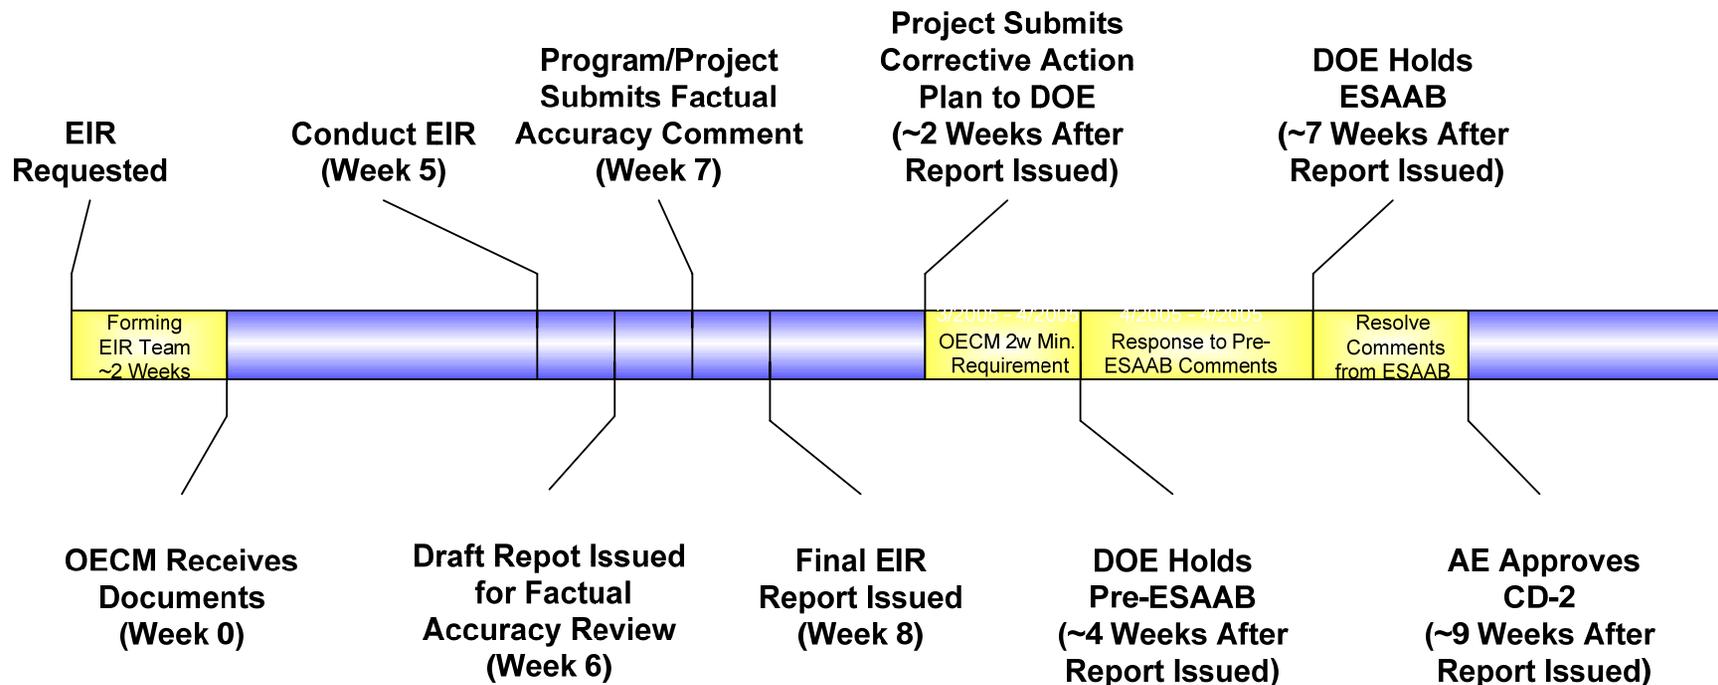




NOvA Project

Draft Critical Design Prerequisites

Updated 16-Jan-07



Estimated Need by Dates for DOE Approvals and Documents

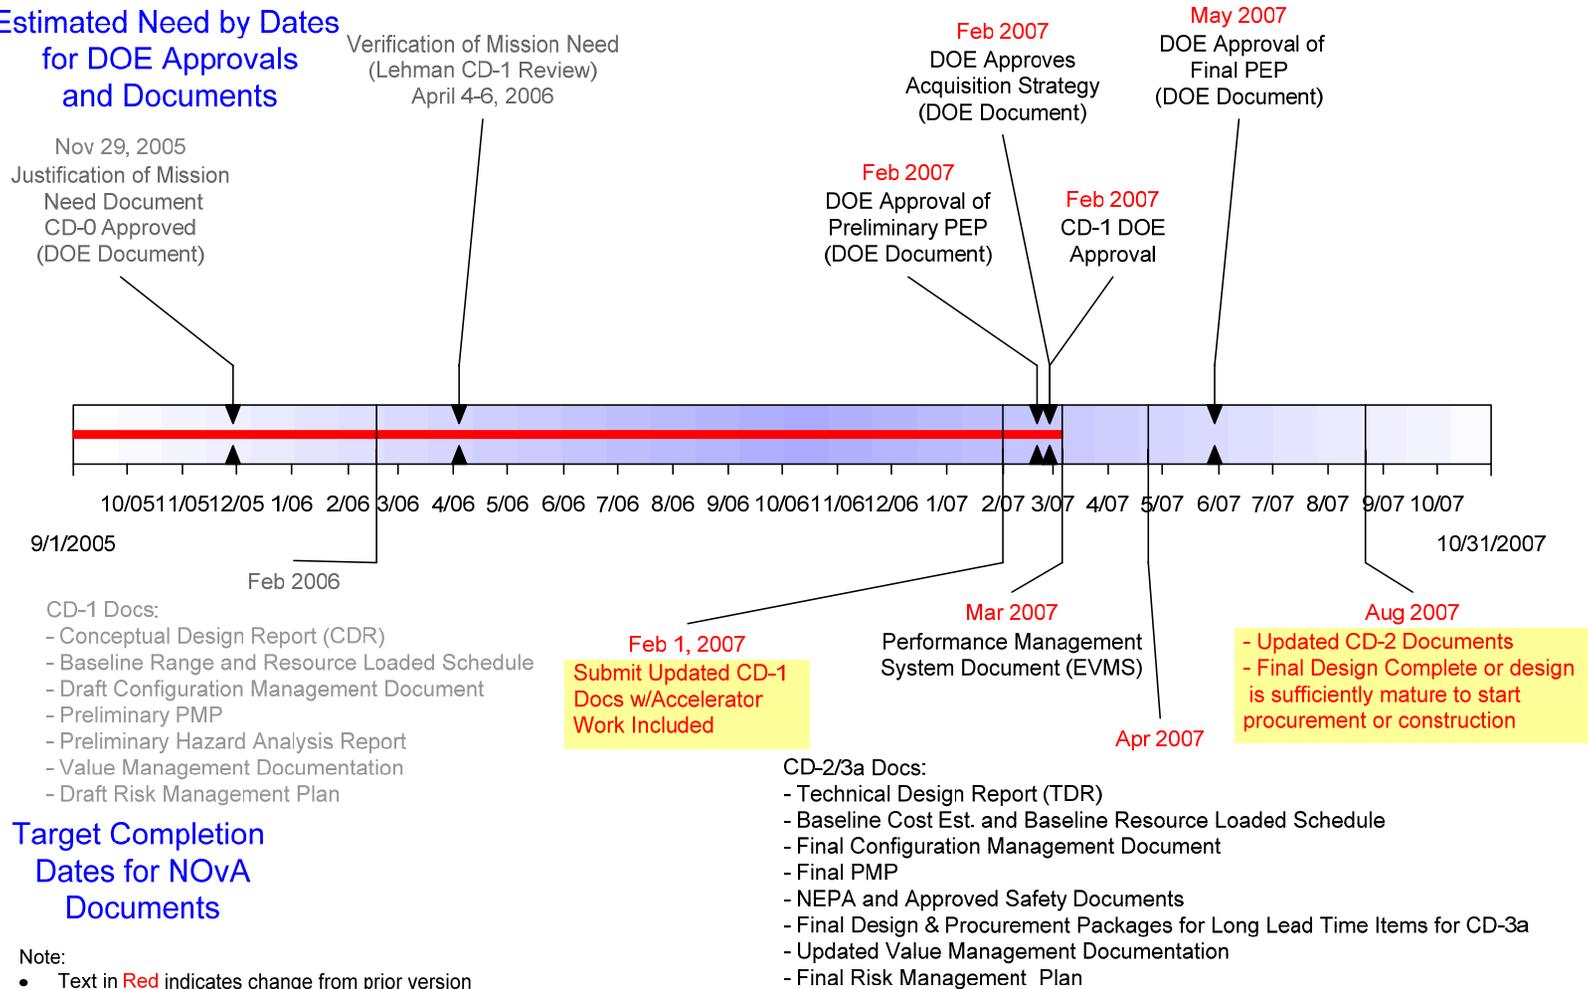


Target Completion Dates for NOvA Documents



NOvA Project Proposal/Cooperative Agreement Draft Process



Updated 05-Feb-07

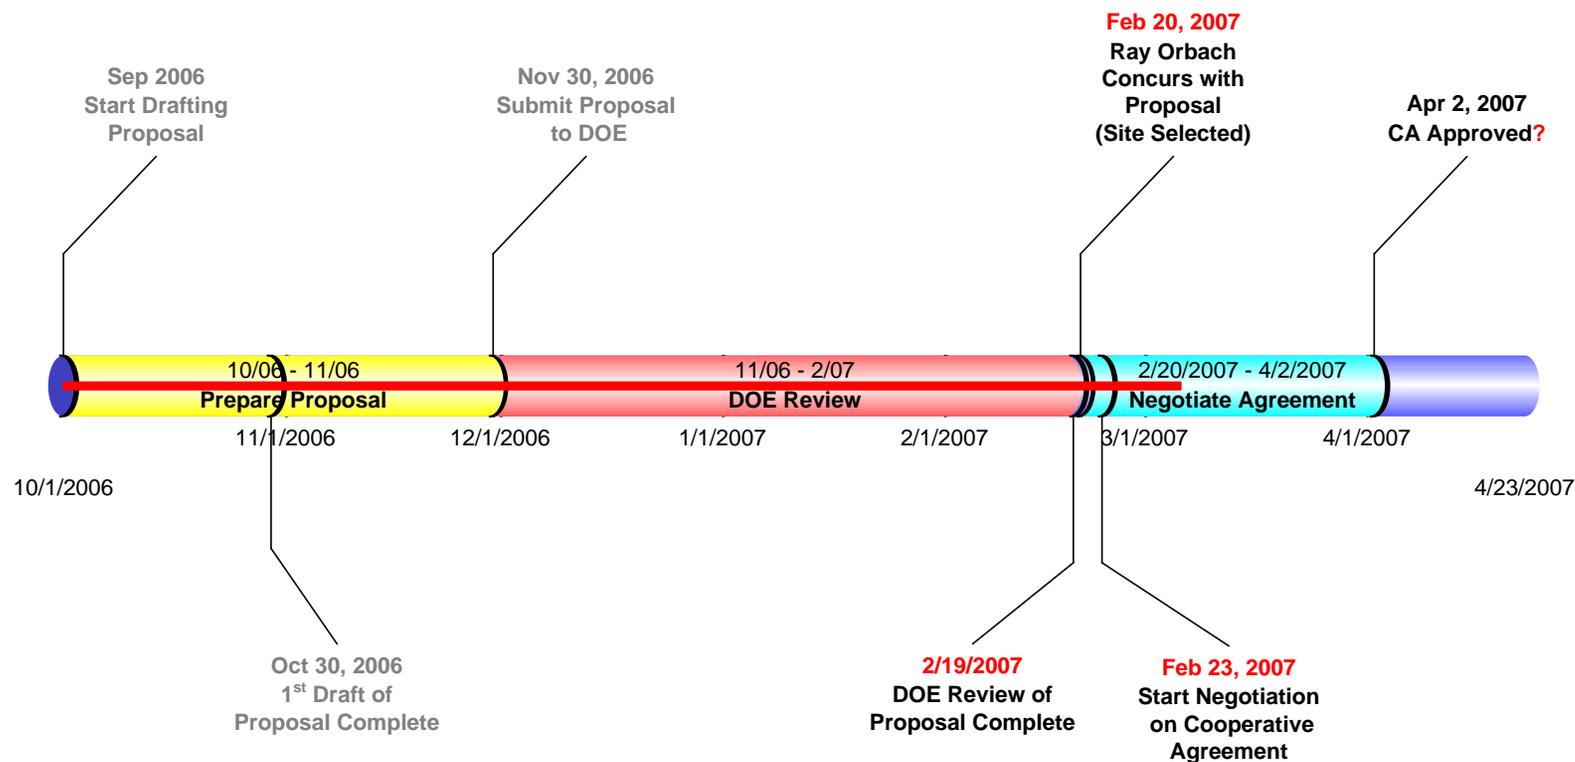

Note:

- Text in **Red** indicates change from prior version

Action Items

New Items:

- a) Near Detector reviewers may continue asking questions of NOvA through Tuesday, 27-Feb and then assemble their comments and email them to John Cooper and Hugh Montgomery by Friday, 2-March [Stephen Pordes, Steve Geer and Chris Laughton]

Rollover Items from Prior Meetings:

- b) Describe how \$1.1M savings in DAQ might be achieved [John Cooper/Ron Ray]
- c) Provide funding profile for use in updated CD-1 documents [Mike Procario/ Thomas Carolan Pepin]
- d) Determine what “CD-3a” strategy is the way to proceed [Hugh Montgomery/John Cooper]
- e) Consider options and determine direction with regard to a Near Detector and housing for such [Hugh Montgomery/John Cooper]
- f) Decide on a Fermilab building to house a NOvA factory [Hugh Montgomery/Jim Strait/John Cooper]
- g) NOvA to develop a scorecard on how the 14 contractor requirements from DOE O 413.3a Attachment 2 are met for the full NOvA project overall and how they are met, as applicable, for the Cooperative Agreement. This scorecard is to be presented at a future NOvA Working Group Meeting. John Cooper/ Ron Ray]
- h) NOvA to document NOvA’s internal procurement/approval process and present at a WGM. [John Cooper/ Ron Ray]
